Thadomal Shahani Engineering College, Bandra
Department of Artificial Intelligence & Data Science

Experiment 06

Date of Performance: 13/09/2026 **Date of Submission: 13/09/2026**

Class: T1

Student Roll No: 34,41,43

Student Name:Ishita Gurbaxani, Lakshya Kanjwani, Yuvraj Keswani

LO Mapped: Build and manage automated CI/CD pipelines for application development, testing, packaging, and deployment.

Aim: To study and Implement Agile Software Project lifecycle using Jira with DevOps Pipeline Integration.

Jira Agile Project Management User Manual

Source Video	Ultimate Jira Tutorial for Beginners	**Instructor**	Stewart Gauld
Project Example	Sheify Website Development (key: SWD)	**Video URL**	youtube.com/watch?v=8jWKwiIcWPI
Tools Used	Jira (Scrum), GitHub	**Sprint**	SWD Sprint 1 (3 Jun – 1 Jul)

1. Account Creation & Initial Setup [00:00 - 02:00]

- **Navigate to Jira:** Visit Jira's official portal and select 'Get Jira for free'.
- **Tier Limits:** Jira Free tier supports up to 10 users, suitable for standard Scrum teams (typically 5 to 9 members).
- **Account Registration:** Enter work email, verify with the security code, input full name, create password, and enter business/organization domain.
- **Work Type Selection:** Select 'Software Development' and choose the 'Scrum' methodology.

2. Project Creation & Team Member Invitations [02:00 - 03:30]

- **Project Name:** Set the project name as 'Sheify Website Development' (project key: SWD).

- **Invite Collaborators:** Navigate to the team icon in the top navigation bar, input collaborator email addresses, configure invite permissions, and click 'Add people'.

3. Work Breakdown Structure & Epic Management [03:40 - 06:40]


The Scrum framework is organized hierarchically into four core layers:

- Roadmap: Top-level strategic project goals.
- Epics: Large initiatives broken into deliverables (managed by Product Owner).
- User Stories: Functional requirement units that deliver customer value.
- Tasks / Sub-tasks: Specific technical tasks completed by developers.

Configured Project Epics

- **Epic 1:** SWD-1 ‘Improve Customer Service’.
- **Epic 2:** SWD-2 ‘Increase Product Page Conversions’.

The List view shows both epics with their assignee, reporter, priority and status. Both start in the To Do status.

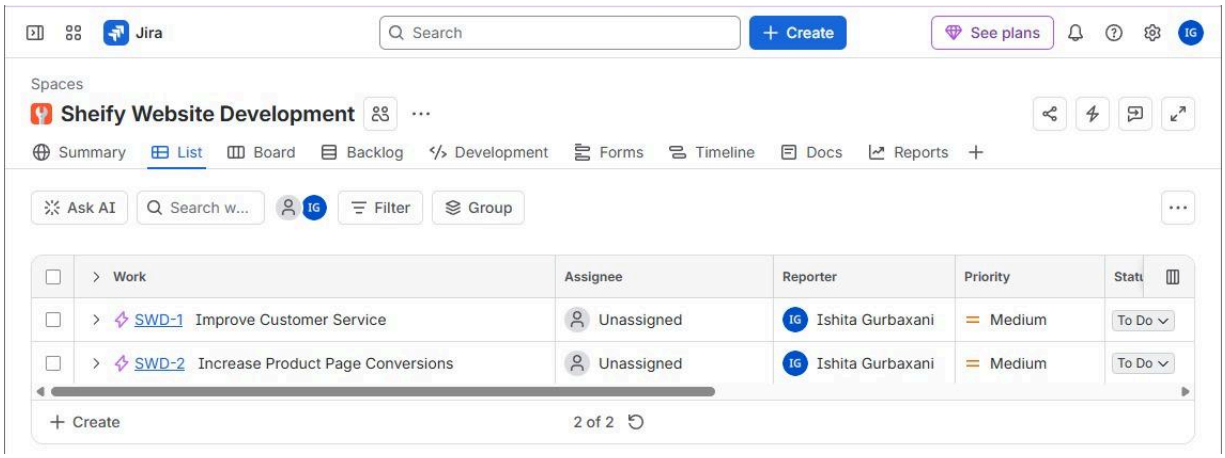


4. Backlog Refinement, Stories & Tasks [06:40 - 09:30]

In the Backlog view, the team creates work items and assigns each one to a parent epic. Items planned for the first iteration sit in the sprint section; the remaining items stay in the Backlog section below it.

Issue Key	Type	Summary / Requirement	Parent Epic
SWD-1	Epic	Improve Customer Service	—
SWD-2	Epic	Increase Product Page Conversions	—
SWD-4	Task	Provide live chat as a feature	SWD-1 Improve Customer Service
SWD-5	Task	Add WhatsApp chat to our website	SWD-1 Improve Customer Service
SWD-6	Task	Add Facebook messenger chat to our website	SWD-1 Improve Customer Service
SWD-7	Story	Create a video based knowledge base	SWD-1 Improve Customer Service
SWD-8	Story	Create a review based system for collecting reviews	SWD-2 Increase Product Page Conversions


Issue Linking & Dependencies


To deliver SWD-4 (‘Provide live chat as a feature’), developers must first complete two blocker tasks. SWD-4 is linked to SWD-5 and SWD-6 with the relationship ‘is blocked by’ (see the Linked work items panel below).

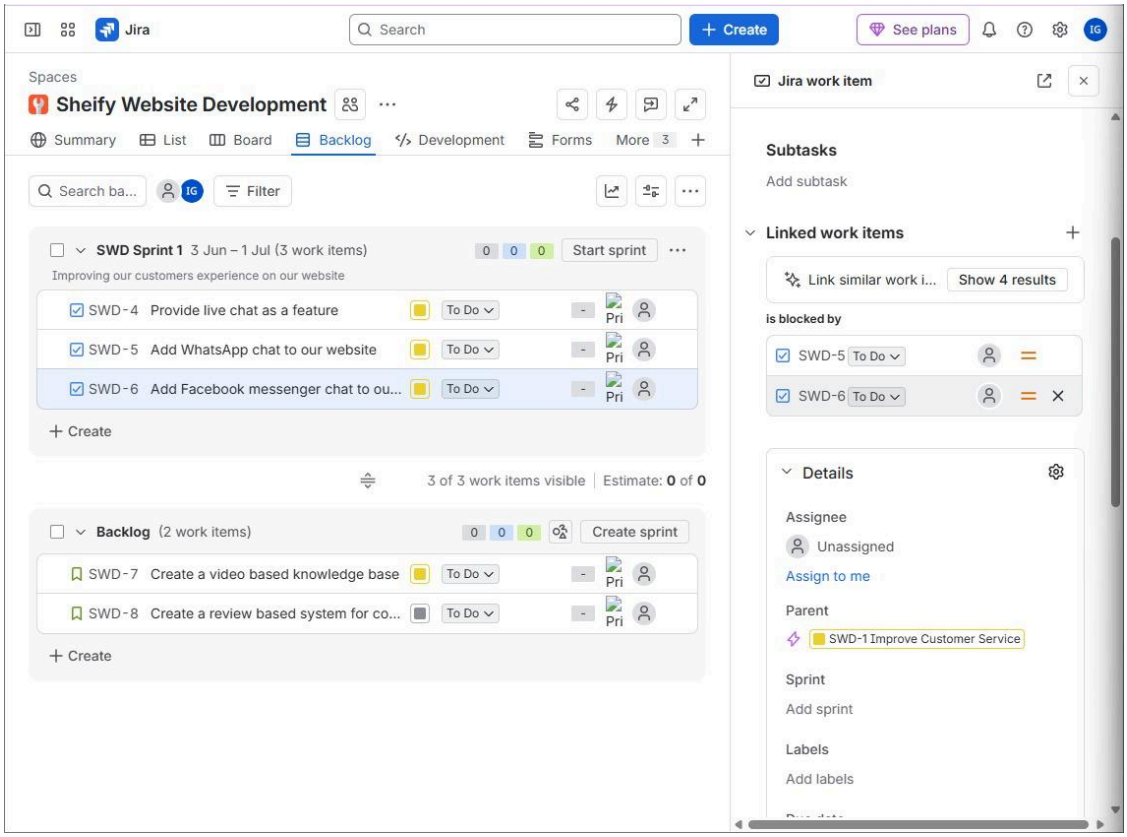

5. Sprint Planning & Starting the Sprint [09:55 - 12:50]


- **Set Sprint Parameters:** Open the sprint and click 'Start sprint'. Enter the sprint name (SWD Sprint 1), choose a custom duration, and set the start date (3 June) and end date (1 July).
- **Sprint Goal:** Improving our customers experience on our website.
- **Move Items into Sprint:** Drag SWD-4, SWD-5 and SWD-6 from the Backlog into SWD Sprint 1 (3 work items).
- **Click Start:** Click ‘Start’ in the dialog. Jira transitions the sprint into the live Active Board and confirms with a ‘Sprint started’ message.

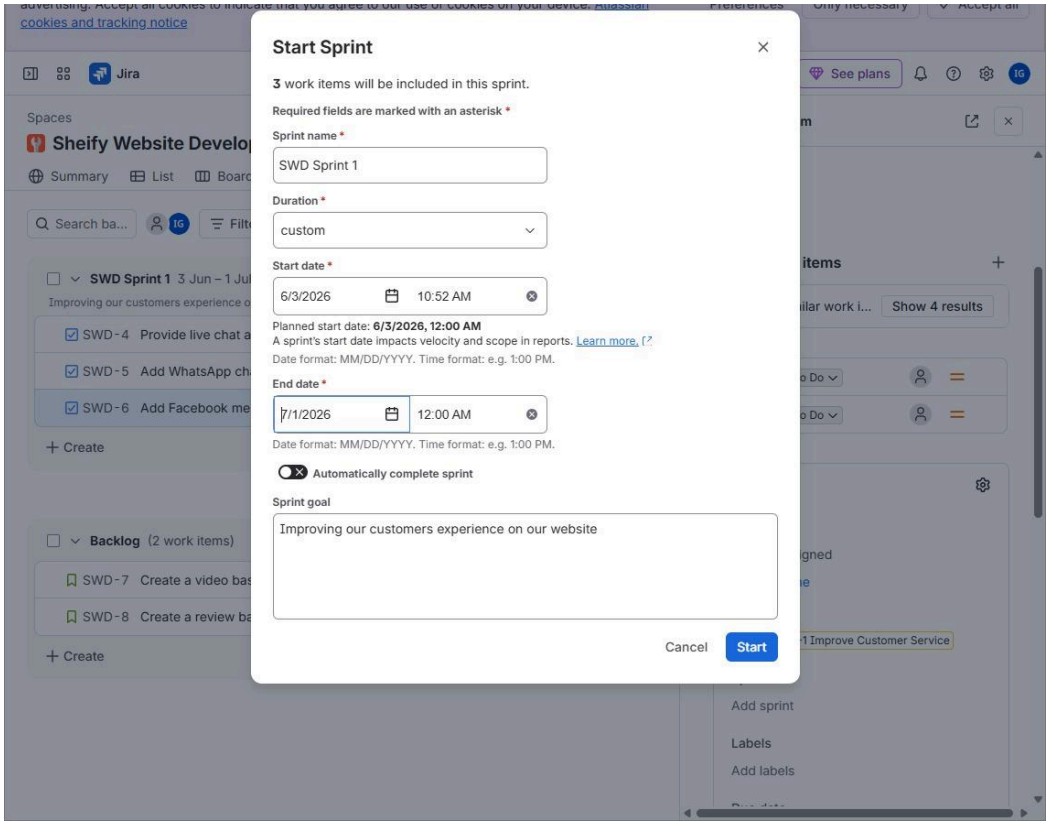
Start Sprint
3 work items will be included in this sprint.
Required fields are marked with an asterisk *
Sprint name *
SWD Sprint 1
Duration *
custom
Start date *
6/3/2026
10:52 AM
Planned start date: 6/3/2026, 12:00 AM
A sprint's start date impacts velocity and scope in reports. Learn more.
Date format: MM/DD/YYYY. Time format: e.g. 1:00 PM.
End date *
7/1/2026
12:00 AM
Date format: MM/DD/YYYY. Time format: e.g. 1:00 PM.
Automatically complete sprint
Sprint goal
Improving our customers experience on our website
Cancel
Start

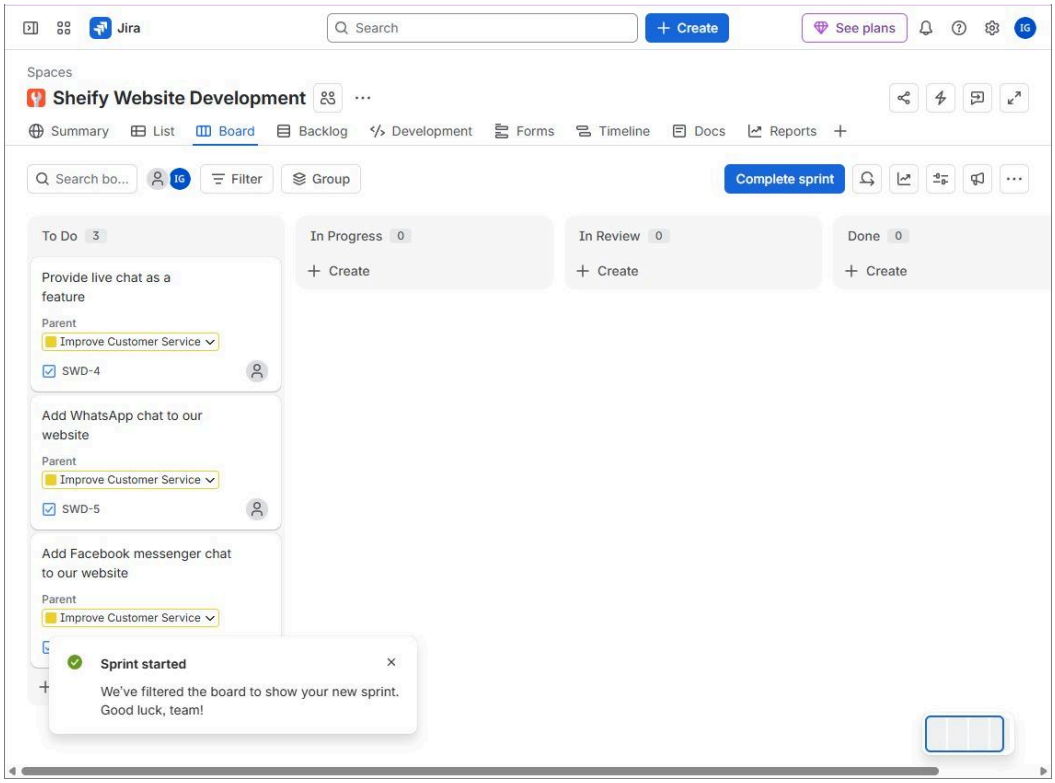
Jira
Search
Create
See plans
Spaces
Sheify Website Development
Summary
List
Board
Backlog
Development
Forms
Timeline
Docs
Reports
Search bo...
Filter
Group
Complete sprint
To Do 3
In Progress 0
In Review 0
Done 0
Provide live chat as a feature
Parent
Improve Customer Service
SWD-4
Add WhatsApp chat to our website
Parent
Improve Customer Service
SWD-5
Add Facebook messenger chat to our website
Parent
Improve Customer Service
Sprint started
We've filtered the board to show your new sprint. Good luck, team!


6. Sprint Execution & Status Progression


As developers pick up work, they drag cards across the board columns: To Do → In Progress → In Review → Done. In this project, SWD-4 moved to In Progress, SWD-5 moved to In Review, and SWD-6 remained in To Do.

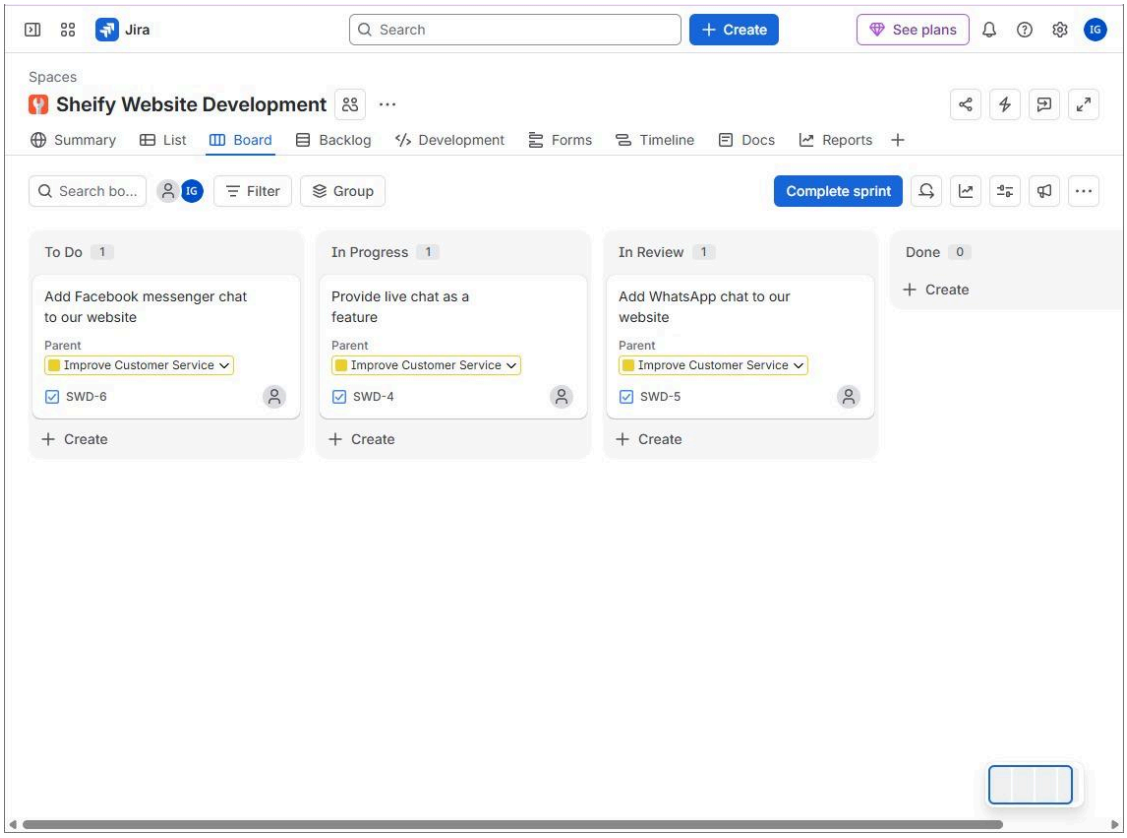

7. Timeline View [11:34 - 13:00]

The Timeline (Gantt-style) view visualizes epics, their child work items, and the sprint across the months. The sprint appears as a bar above the epics, and each epic shows a progress bar of its child items by status.

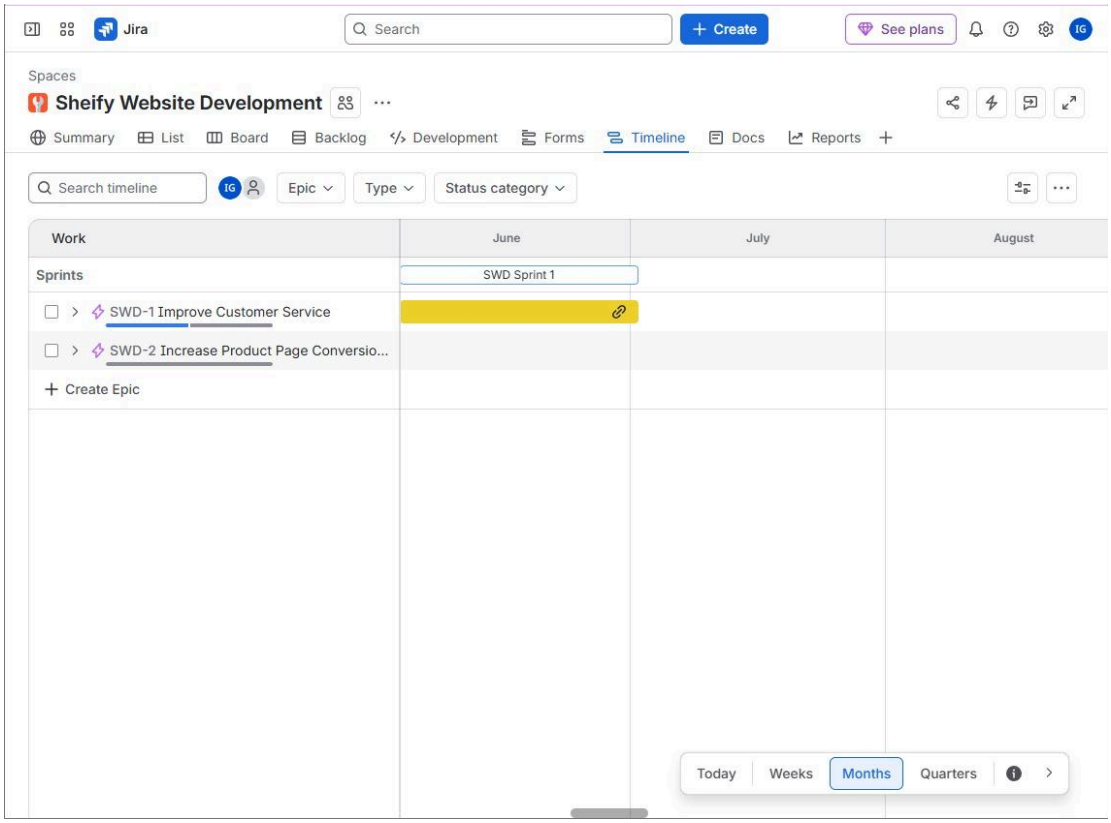

Jira
Search
Create
See plans
Spaces
Sheify Website Development
Summary
List
Board
Backlog
Development
Forms
Timeline
Docs
Reports
Search timeline
Epic
Type
Status category
Work
June
July
August
Sprints
SWD Sprint 1
SWD-1 Improve Customer Service
SWD-2 Increase Product Page Conversio...
Create Epic
Today
Weeks
Months
Quarters

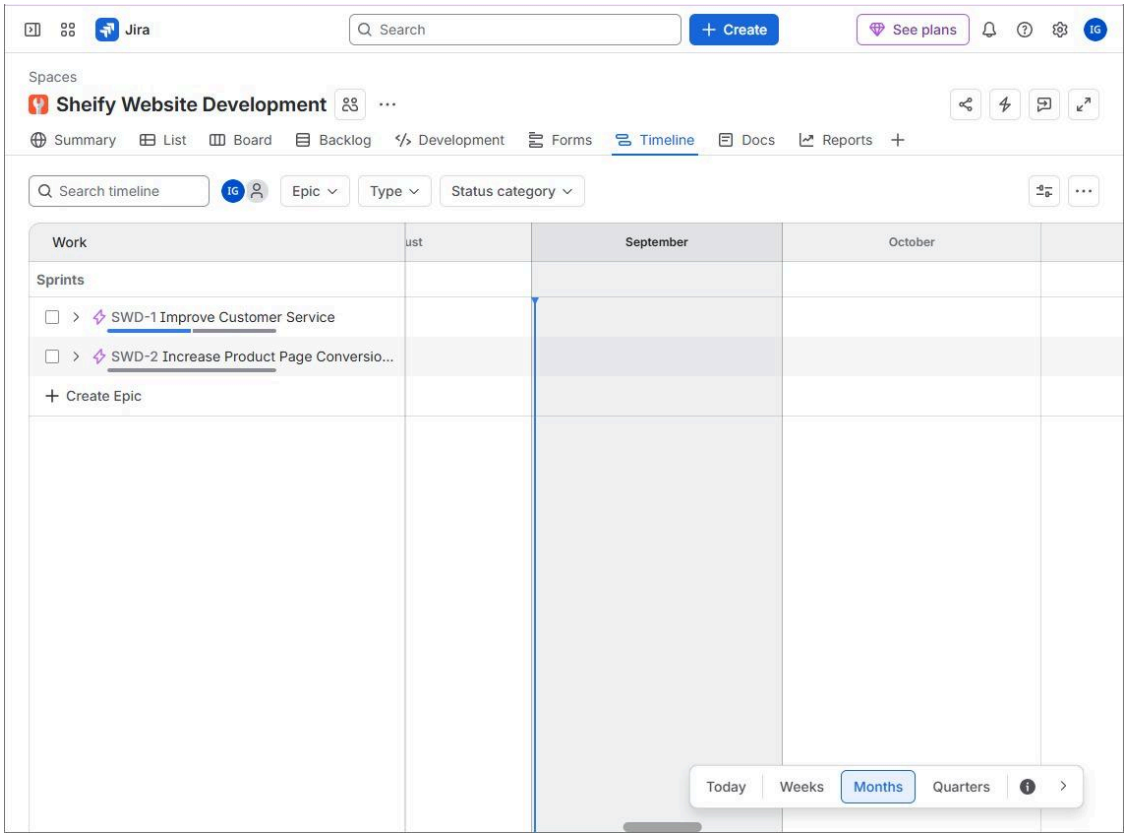

Jira
Search
Create
See plans
Spaces
Sheify Website Development
Summary
List
Board
Backlog
Development
Forms
Timeline
Docs
Reports
Search timeline
Epic
Type
Status category
Work
September
October
Sprints
SWD-1 Improve Customer Service
SWD-2 Increase Product Page Conversio...
Create Epic
Today
Weeks
Months
Quarters


8. GitHub Integration & Development Panel

Jira can be connected to GitHub so that code activity appears on the work item. The key step is to include the Jira issue key (for example SWD-5) in the commit message.

- **Create the change:** In the GitHub repository (Sheify-Website-Development), edit or add a file on the main branch and click ‘Commit changes’.
- **Name the commit with the issue key:** Enter a commit message that starts with the key, e.g. ‘SWD-5: added WhatsApp chat integration’, then confirm the commit.
- **Check the repository:** The new commit appears at the top of the file list with its short hash.
- **Check Jira:** Open the work item’s Development panel and select the Commits tab. The commits are listed automatically.

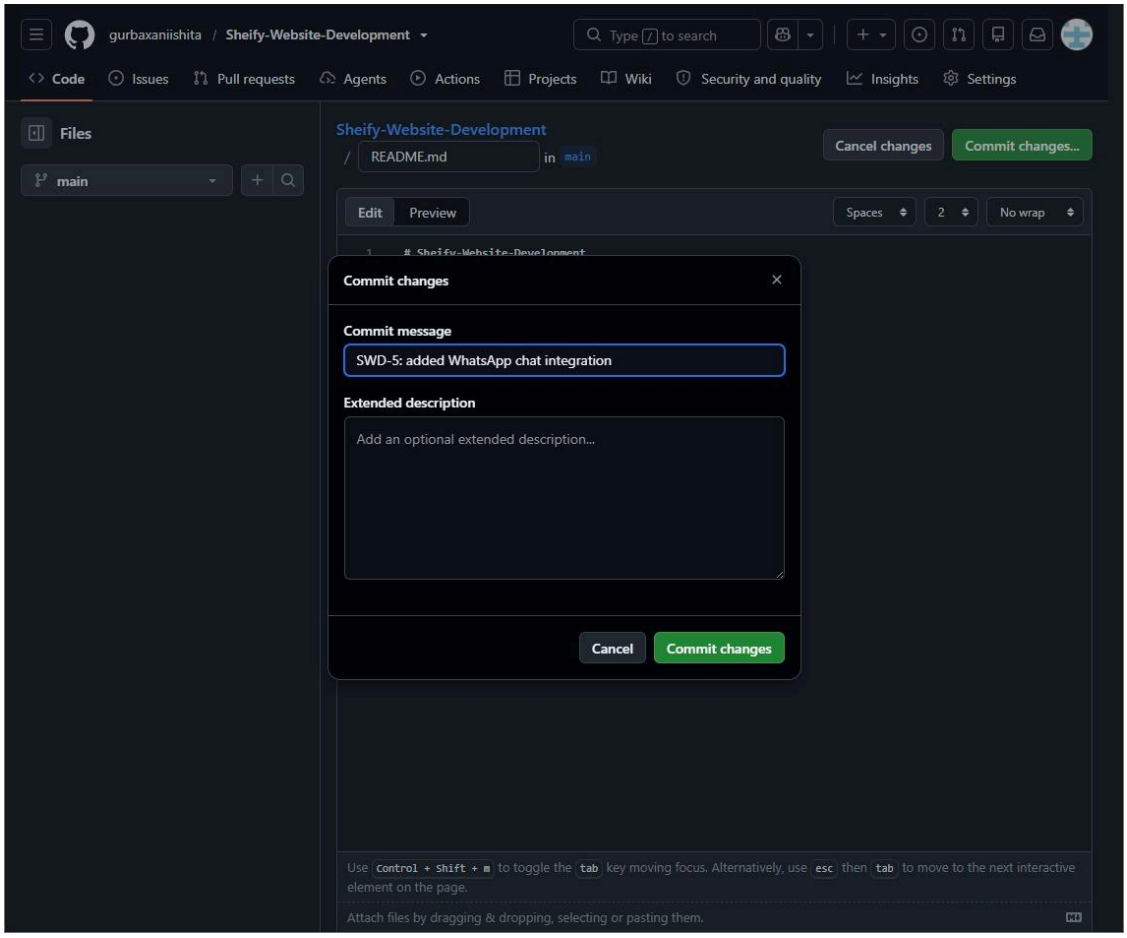


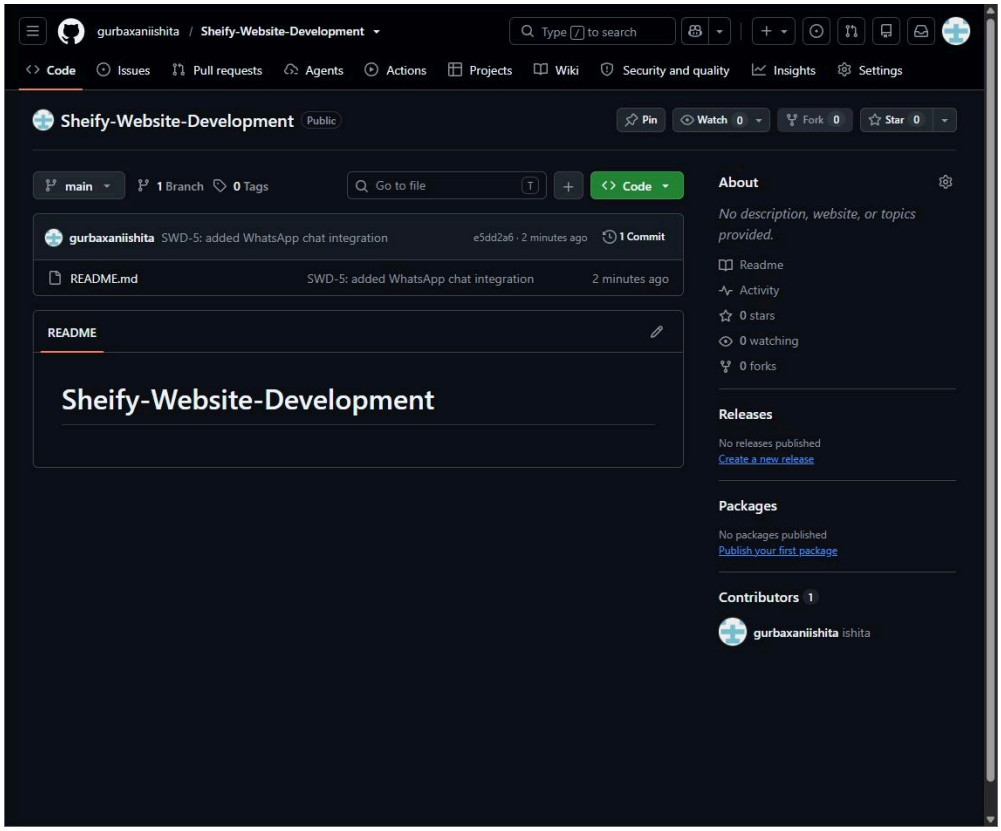

gurbaxaniishita / Sheify-Website-Development
Type / to search
Code
Issues
Pull requests
Agents
Actions
Projects
Wiki
Security and quality
Insights
Settings
Sheify-Website-Development
Public
Pin
Watch 0
Fork 0
Star 0
main
1 Branch
0 Tags
Go to file
Code
gurbaxaniishita SWD-5: added WhatsApp chat integration
e5dd2a6 · 2 minutes ago
1 Commit
README.md
SWD-5: added WhatsApp chat integration
2 minutes ago
README
Sheify-Website-Development
About
No description, website, or topics provided.
Readme
Activity
0 stars
0 watching
0 forks
Releases
No releases published
Create a new release
Packages
No packages published
Publish your first package
Contributors 1
gurbaxaniishita ishita

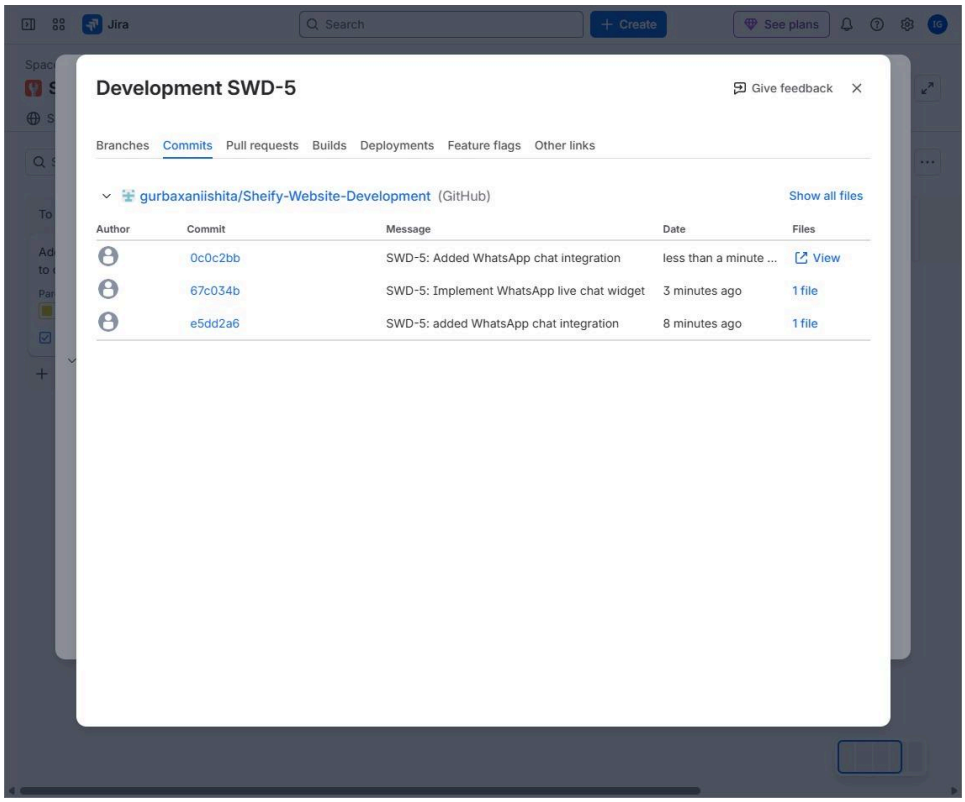
Jira
Search
Create
See plans
Development SWD-5
Give feedback
Branches
Commits
Pull requests
Builds
Deployments
Feature flags
Other links
gurbaxaniishita/Sheify-Website-Development (GitHub)
Show all files
Author
Commit
Message
Date
Files
0c0c2bb
SWD-5: Added WhatsApp chat integration
less than a minute ...
View
67c034b
SWD-5: Implement WhatsApp live chat widget
3 minutes ago
1 file
e5dd2a6
SWD-5: added WhatsApp chat integration
8 minutes ago
1 file

9. Dashboards & Gadgets [13:30 - 15:00]

Dashboards give the team an at-a-glance summary using gadgets. The SWD Sprint 1 dashboard includes an Activity Stream (a live log of status changes, sprint updates, parent changes and issue links), a Sprint Burndown Gadget, a Sprint Health Gadget, a Pie Chart by assignee, and an Assigned to Me gadget.

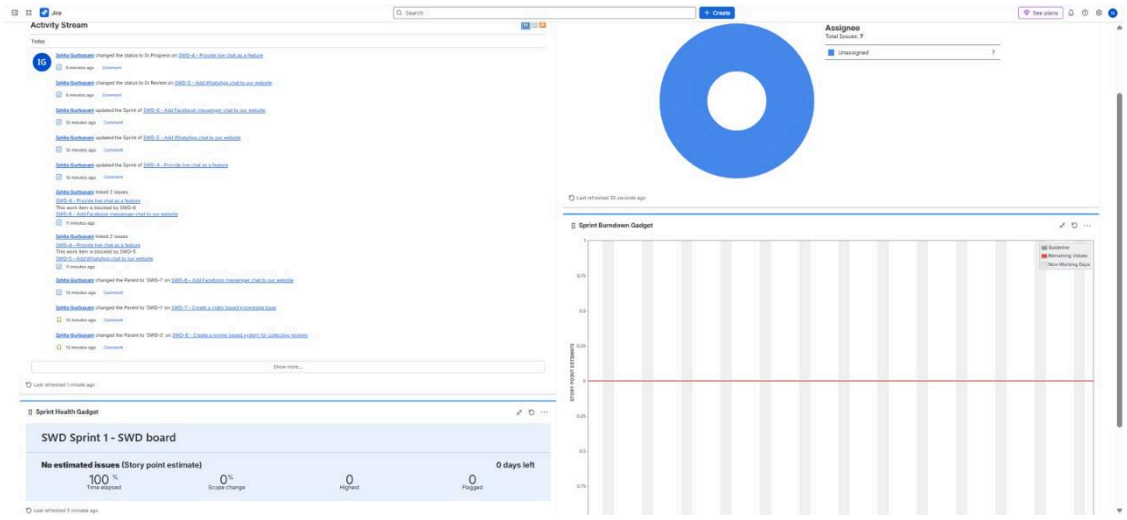

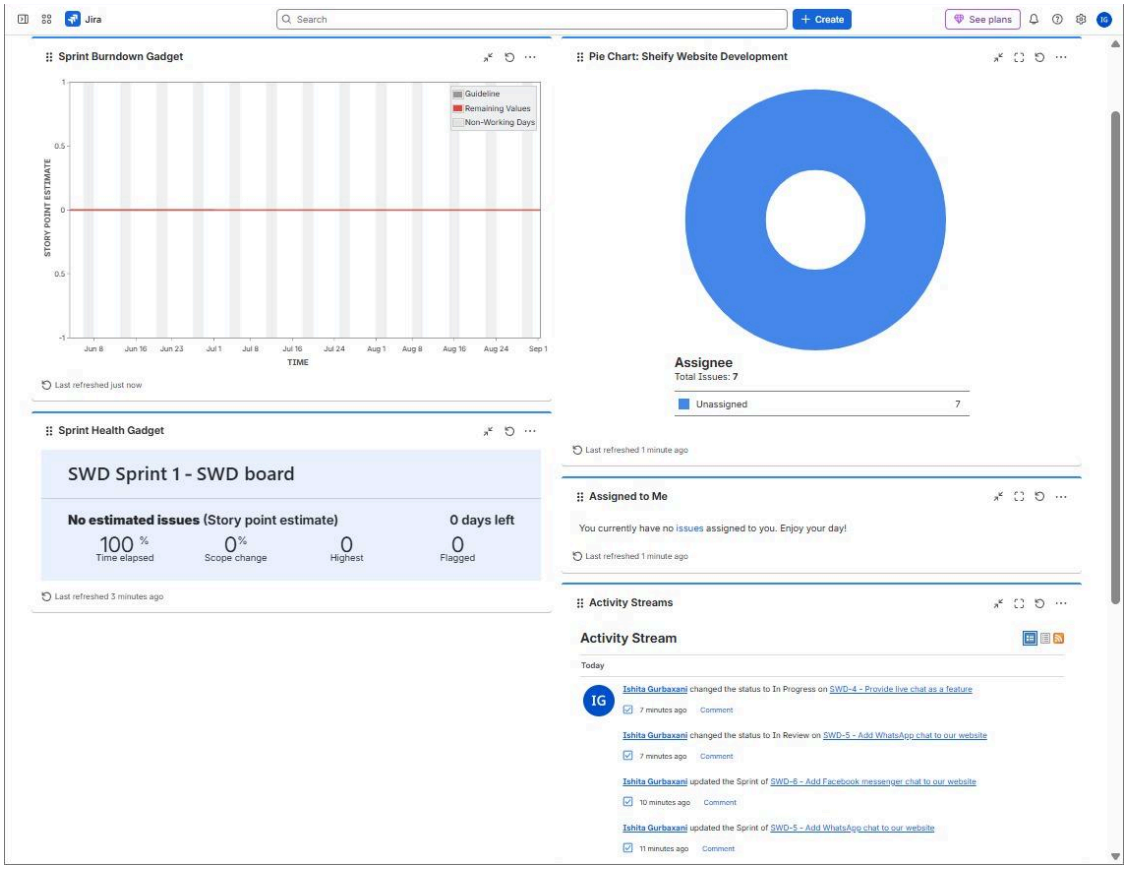


Reading the gadgets

The burndown and sprint health gadgets show no values because the work items have no story point estimates. Add estimates to the items to get a meaningful burndown line.

10. Reports [15:00 - 15:30]

The Reports tab summarizes project data: work items by status, type and assignee, plus the work item creation trend and cycle time. In this project the project has 7 work items (Tasks, Stories and Epics), all unassigned.

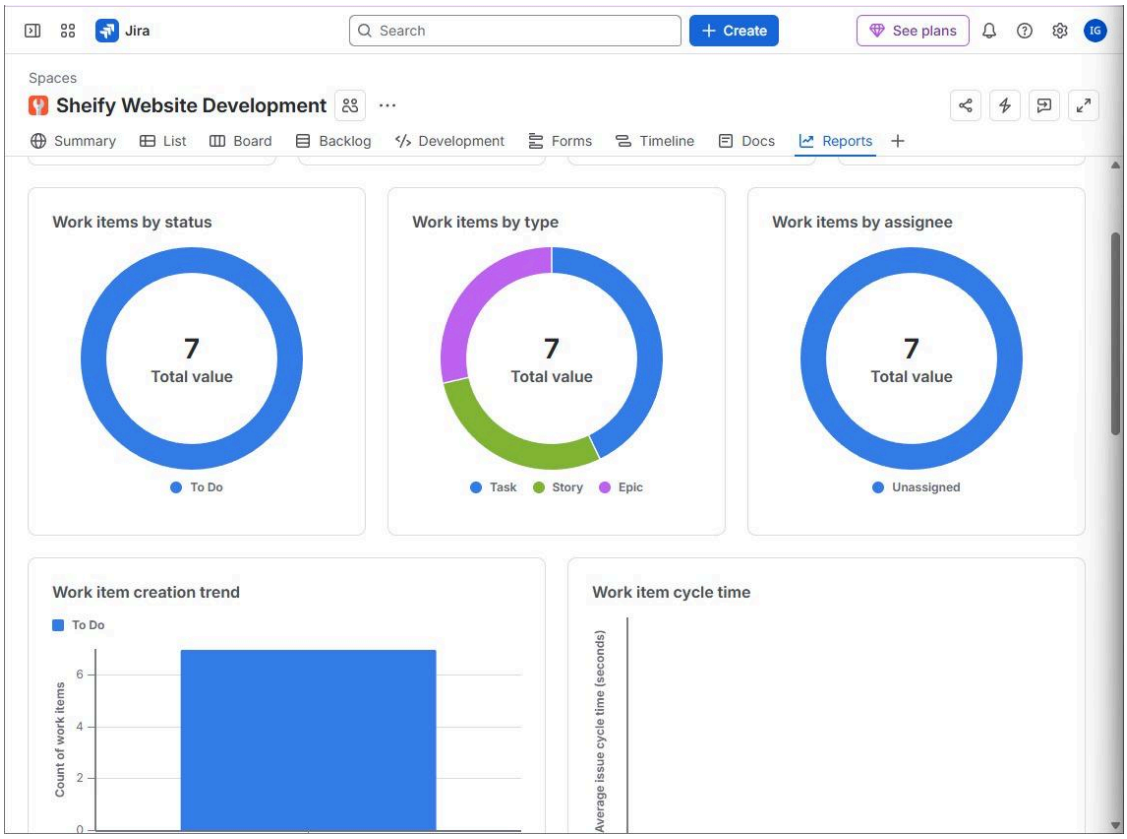

11. Other Integrations

- **Project Pages & Retrospectives:** Integrated Confluence spaces for team sprint retrospectives.
- **App Integrations:** Third-party apps such as Slack, Google Forms and TimeCamp (time tracking) can be connected to Jira.
